

SPRINT 1 · JUN 1 – JUN 5, 2026

Sprint 1 Review

Goal: transition infrastructure ownership from the offshore team to Reform-A.i.

● SPRINT HEALTH: GREEN · GOAL ACHIEVED

SPRINT GOAL

Achieved

Infra transition landed

COMPLETION

45%

13 of 29 work items

CARRIED OVER

16

Deprioritized by design

OPEN BLOCKERS


0

All clear

The Headline

We set out to move our infrastructure in-house, and we did it. The core transition off the offshore (Asymmetri) team to Reform-A.i landed (RAI-552), backed by Google Cloud Secret Manager (RAI-559) and per-push code versioning (RAI-624). That foundational work ran heavier than estimated, so we made a deliberate call: protect the goal and consciously push lower-priority stories to Sprint 2. The result is a lower raw completion number that represents a *won* sprint, not a missed one.

Delivery at a Glance

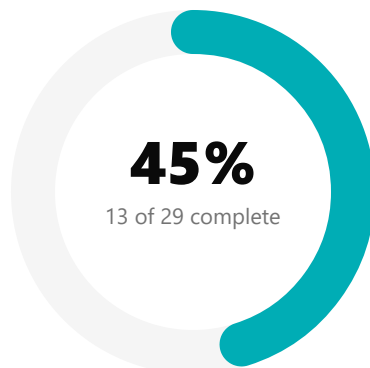

Infrastructure — the goal

2 / 2

Tech Debt

2 / 3

Product (Stories + Bugs)

9 / 24

By work type: Bugs 8 / 16 done · Stories 5 / 13 done. Bugs led delivery while the team focused capacity on the infrastructure stories.

What We Shipped

RAI-552

Infrastructure moved to Reform-A.i

Infrastructure · Goal

RAI-559

GCP Secret Manager + centralized env vars

Tech Debt

RAI-624

Per-push code-set version control

Infrastructure

RAI-594

DB-backed legal documents with Admin UI

Tech Debt

Plus production fixes: Partner Projects errors, Spanish localization, contract creation, and the seller/supplier user-type bug — 13 items completed in total.

How We're Self-Correcting

Retro action items

Document Slack/Jira ticket-submission process



Research automated testing (Cypress)



Research user-tracking tooling



GitHub/Jira integration



Implement code review in GitHub



Process improvements next sprint

- Adopt t-shirt sizing on every item for real capacity planning
- Budget goal-work capacity first, then add stories
- Add release rollback capability (already queued in Sprint 2)
- Surface and clear blockers mid-sprint, not at close
- Record the sprint goal in Jira for automatic health

Risk Watch

No open blockers. Every Sprint 1 item is either shipped or actively in flight heading into Sprint 2 — a clean handoff.

Sprint 2 Planning

JUN 9 – JUN 15, 2026

Goal: Wompi Account Update & Dashboard Views

COMMITTED

28

19 stories / 9 bugs

SIZED

28 / 28

all sized

CARRYOVER

16


12 net-new

READINESS

Ready

gate passed

Committed Scope

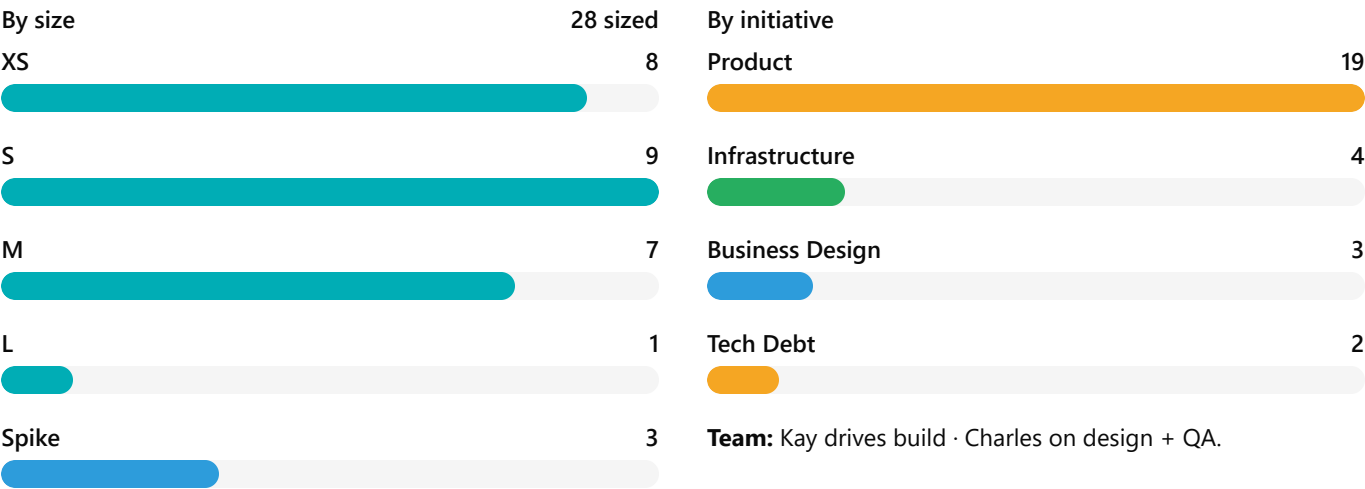

Planning Watch

16 of 28 items are carryover from Sprint 1 — 12 are net-new. Sprint 2 is largely about finishing the work that was deliberately deprioritized to land Sprint 1's goal. Watch for piling new scope on top of the carryover backlog.

SPRINT 2

What's in Scope

All 28 committed items — every story and bug, ordered by progress. **CO** = carryover from Sprint 1.

Business Design (3)

KEY	SIZE	STATUS	OWNER	SUMMARY
RAI-546	L	To Do	Charles	Design for Supplier Catalogs
RAI-625	M	To Do	Charles	Design Creating a Project from the Visualization
RAI-628	M	To Do	Charles	Research other tools to track how users interact with platform

Product (19)

KEY	TYPE	SIZE	STATUS	OWNER	SUMMARY
RAI-437	Story	S	QA	Charles	Create Home Seller User Type
RAI-547	Story	S	QA	Charles	CO Help Centre
RAI-593	Bug	XS	QA	Kay	CO Quick Jobs: Wallpaper option + optional measurements
RAI-605	Bug	XS	QA	Kay	CO Prod: SP profile showing specialties in English
RAI-613	Bug	XS	QA	Charles	CO Update Materials in Project to Spanish
RAI-619	Bug	XS	QA	Charles	CO Bid estimated value rounding issue
RAI-548	Story	S	In Prog	Kay	CO FAQ
RAI-601	Bug	XS	In Prog	Kay	CO Seller Module: Before/After photos not showing
RAI-610	Story	S	In Prog	Kay	CO Review and suggest for the Landing Pages
RAI-608	Story	M	To Do	Kay	Update Wompi Account to New ReformAI Bank Account
RAI-622	Story	S	To Do	Kay	Update Broker Agreement for White Glove Service
RAI-550	Bug	XS	To Do	Kay	Service Providers: Update Subscription
RAI-124	Story	M	To Do	Kay	CO Dashboard
RAI-148	Story	S	To Do	Kay	CO Dashboard
RAI-23	Story	S	To Do	Kay	CO Dashboard
RAI-65	Story	M	To Do	Kay	CO Teams
RAI-592	Bug	XS	To Do	Kay	CO Remove Moodboards from Homeowner Subscription
RAI-602	Bug	S	To Do	Kay	CO Distressed Assets: restore 3-tier photo option
RAI-607	Bug	XS	To Do	Kay	CO Inspiration Hub: Style Filter not working

Tech Debt (2)

KEY	TYPE	SIZE	STATUS	OWNER	SUMMARY
RAI-582	Story	S	In Prog	Kay	CO [LOGIC] Migrate hardcoded filter prices/ranges to DB
RAI-579	Story	M	To Do	Kay	[DATA] Automated DB migration pipelines and rollback strategies

Infrastructure (4)

KEY	TYPE	SIZE	STATUS	OWNER	SUMMARY
RAI-467	Story	M	To Do	Kay	GCP: Install a function to determine cost per API call
RAI-623	Story	Spike	To Do	Kay	Analysis Task: Web Scraper for Seller Module
RAI-626	Story	Spike	To Do	Kay	Automate the pipeline to Jira to connect each Story/Bug with versioning
RAI-627	Story	Spike	To Do	Kay	Implement Code Review in GitHub
