

SPRINT 2 · JUN 2026

Revisión Sprint 2

Objetivo: cambiar la facturación de Wompi a la cuenta de ReformAI y entregar los 3 tableros de usuario.

● ESTADO DEL SPRINT: VERDE · OBJETIVO PARCIAL

OBJETIVO

Parcial

Tableros sí; Wompi
pendiente

COMPLETADO

72%

29 de 40 ítems

TRASLADADO

11

Pasan al Sprint 3

MEJOR A LA FECHA

72%

Mayor completado hasta
ahora

Lo Más Importante

El sprint más fuerte hasta la fecha - 29 de 40 (72%). Los 3 tableros de usuario se entregaron. El cambio de la cuenta Wompi sigue pendiente por parte de Wompi - una dependencia externa, no una falla del equipo (el CEO se reunió con Wompi y el cambio pasa al Sprint 3). **Destacado:** el análisis estaba previsto solo como tarea de investigación; el equipo encontró PostHog y lo implementó por completo dentro del sprint, adelantándose al plan.

Entrega de un Vistazo



Por iniciativa

Producto

20 / 25

Infraestructura

5 / 8

Diseño de Negocio

4 / 5

Deuda Técnica

0 / 2

Por tipo: Bugs 13 / 15 · Historias 15 / 24. La deuda técnica se quedó atrás (0 de 2).

Lo Que Entregamos y Por Qué Importa

TABLEROS

3 tableros de usuario en vivo

Objetivo

POSTHOG

Análisis encontrado + implementado en el sprint

Adelanta el plan

SALUD OPS

Nuevo tablero de salud operativa

Infraestructura

CORREOS

Plantillas de notificación para cada tipo de usuario

Diseño este sprint

LOGS ADMIN

Registros de actividad de usuario en el módulo admin

Producto

PLATAFORMA


Páginas de aterrizaje en vivo + notificaciones por correo

Producto

La Historia Detrás de los Números

- **Secuela de Cloudflare -> un nuevo tablero.** Referencias de cuentas antiguas que quedaron de la migración de infraestructura del Sprint 1 dañaron las imágenes en producción y costaron un esfuerzo no planeado significativo. Ese dolor inspiró el tablero de salud operativa - ahora se entrega a Kay para llevarlo a producción.
- **El bug de registro con Google** consumió mucho tiempo (corrección esperada para fin de día) - un motor real del trabajo trasladado.
- **El módulo de vendedor (de UAT)** está bloqueado esperando decisión del CEO: actualización del acuerdo de corretaje + precios del servicio White-Glove. Seguirá trasladándose hasta que esa decisión llegue.

Velocidad - Completado por Tamaño

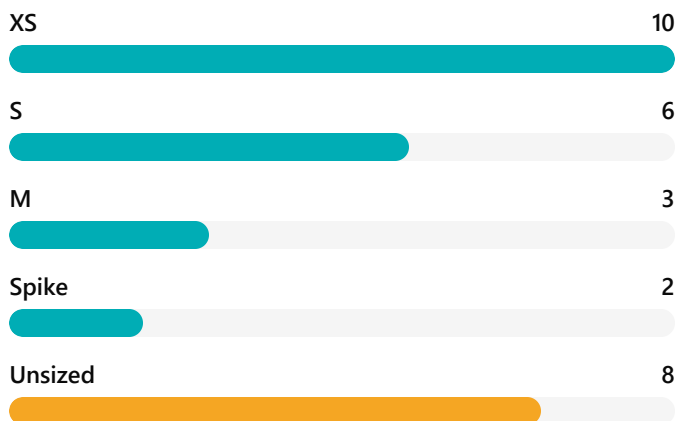

Primera línea base con tamaños

El equipo entregó **21 ítems con tamaño** (10 XS, 6 S, 3 M, 2 Spike) más 8 trasladados sin tamaño. **No se completó ningún L o mayor.** Esta es la primera línea base de rendimiento; se afina con cada sprint totalmente dimensionado.

Cómo Nos Auto-Corregimos

De la retro

- To allocate dedicated time / open bugs for production
- sprints being only 1 week is tight especially in the summer time with holidays, move to 2 week sprint but still have weekly production releases as well as any hot fixes necessary

Acciones próximo sprint

- Desbloquear el módulo de vendedor (CEO: acuerdo de corretaje + precios White-Glove)
- Proteger capacidad para deuda técnica (0/2 este sprint)
- Tiempo dedicado a bugs de producción

Planeación Sprint 3

SPRINT DE FORTALECIMIENTO TÉCNICO

Completar el cambio de Wompi, llevar a producción el tablero de salud operativa, agregar salud de GCP, montar revisión de código + Jira/GitHub - y entregar "crear un proyecto desde una visualización".

COMPROMETIDO

40

11 traslado · 12 nuevos

PREPARACIÓN

Listo

filtro aprobado

DIMENSIONADO

40/40


todo con tamaño

OBJETIVO

Definido

Wompi + técnico

Alcance Comprometido

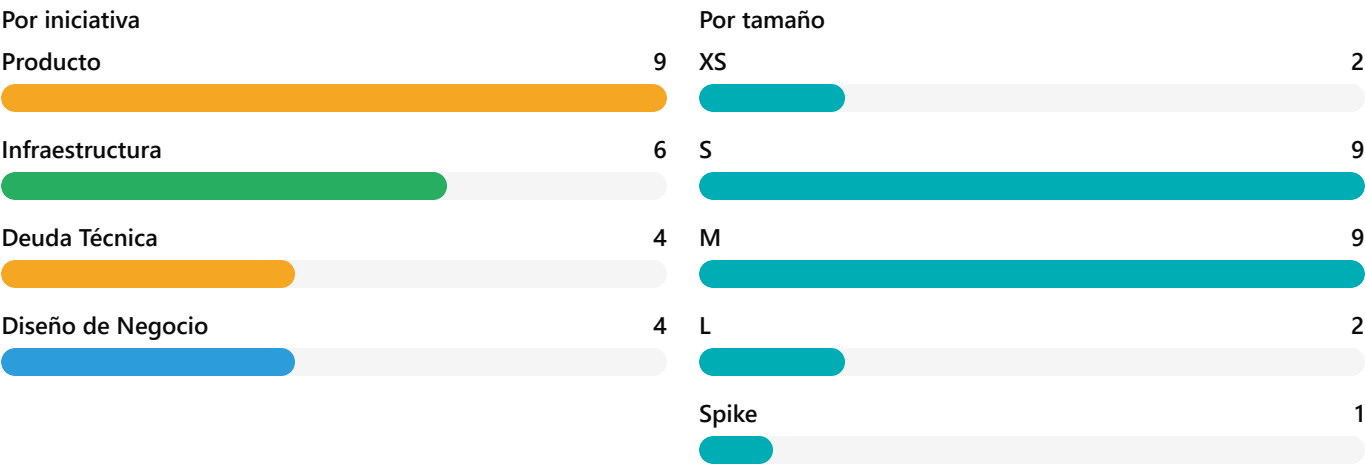

Capacidad vs Sprint Anterior

Alerta de capacidad. El Sprint 3 compromete 9 M y 2 L; el Sprint 2 entregó 3 M y 0 L. La mezcla comprometida es más pesada que el rendimiento comprobado - confirme la capacidad o reduzca los ítems grandes antes de cerrar. La línea base de velocidad tiene un sprint de antigüedad y está parcialmente sin tamaños, trátela como referencial.

SPRINT 3

Qué Está en el Alcance

Los 40 ítems comprometidos. co = trasladado del Sprint 2.

Diseño de Negocio (4)

CLAVE	TIPO	TAMAÑO	ESTADO	RESPONSABLE		RESUMEN
RAI-546	Story	L	En Curso	Charles	co	Design for Supplier Catalogs
RAI-646	Story	M	Por Hacer	David		Design Notification Emails
RAI-649	Story	M	Por Hacer	Charles		Web Scraper to Hubspot Integration Setup
RAI-654	Story	L	Por Hacer	Charles		Moodboard Design

Producto (9)

CLAVE	TIPO	TAMAÑO	ESTADO	RESPONSABLE		RESUMEN
RAI-437	Story	S	QA	Charles	co	Create Home Seller User Type
RAI-65	Story	M	QA	Kay	co	Teams
RAI-608	Story	M	Por Hacer	Kay	co	Update Wompi Account to New ReformAI Bank Account
RAI-550	Bug	XS	Por Hacer	Kay	co	Service Providers: Update Subscription
RAI-650	Story	XS	Por Hacer	Kay		Admin Dashboard Updates
RAI-652	Story	S	Por Hacer	Kay		Bring back version of being able to scroll the platform without being...
RAI-653	Story	S	Por Hacer	Charles		Test Team member functionality
RAI-622	Story	S	Por Hacer	Kay	co	Update Broker Agreement for White Glove Service in Legal Documents an...
RAI-656	Story	M	Por Hacer	Kay		Review and Implement Creating a Project from Visualization

Deuda Técnica (4)

CLAVE	TIPO	TAMAÑO	ESTADO	RESPONSABLE		RESUMEN
RAI-582	Story	S	En Curso	Kay	co	[LOGIC] Migrate hardcoded filter prices and ranges to database for mu...
RAI-560	Story	S	En Curso	Kay	co	[Infra] Implement production error monitoring and alerting for Google...
RAI-587	Story	M	Por Hacer	Kay		[TESTING] Implement automated test coverage for Wompi payment integra...
RAI-648	Story	M	Por Hacer	Kay		Optimize and Implement Operations Health Dashboard

Infraestructura (6)

CLAVE	TIPO	TAMAÑO	ESTADO	RESPONSABLE		RESUMEN
RAI-630	Bug	S	En Curso	Kay	co	Sign in with Google: If user hasn't registered before then need to ta...
RAI-651	Story	S	Por Hacer	Kay		Optimize photos loading: Inspiration Hub and Renovation Game
RAI-467	Story	M	Por Hacer	Kay		GCP: Install a function to determine cost per API call
RAI-579	Story	M	Por Hacer	Kay	co	[DATA] Establish automated database migration pipelines and rollback...
RAI-627	Story	Spike	Por Hacer	Kay	co	Implement Code Review in Github
RAI-644	Story	S	Por Hacer	Kay		Implement Github/Jira Connection

SPRINT 2 · JUN 2026

Sprint 2 Review

Goal: switch Wompi billing to the ReformAI account and ship the 3 user dashboards.

● SPRINT HEALTH: GREEN · GOAL PARTIAL

SPRINT GOAL

Partial

Dashboards yes; Wompi pending

COMPLETION

72%

29 of 40 items

CARRIED OVER

11

Roll into Sprint 3

BEST YET


72%

Highest completion to date

The Headline

Strongest sprint to date - 29 of 40 done (72%). The 3 user dashboards shipped. The Wompi account switch is still pending on Wompi's side - an external dependency, not a team miss (the CEO met Wompi and the switch carries into Sprint 3). **Standout:** analytics was scoped only as a research task; the team found PostHog and fully implemented it in-sprint, ahead of plan.

Delivery at a Glance

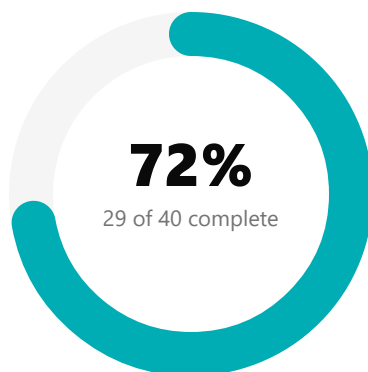

By initiative

Product 20 / 25

Infrastructure 5 / 8

Business Design 4 / 5

Tech Debt 0 / 2

By type: Bugs 13 / 15 done · Stories 15 / 24 done. Tech Debt slipped (0 of 2).

What We Shipped & Why It Matters

DASHBOARDS

3 user dashboards live

Goal

POSTHOG

Analytics found + shipped in-sprint

Ahead of plan

OPS HEALTH

New operational health dashboard

Infrastructure

EMAIL

Notification templates for every user type

Visuals this sprint

ADMIN LOGS

User activity logs in the admin module

Product

PLATFORM


Landing pages live + email notifications

Product

The Story Behind the Numbers

- **Cloudflare fallout -> a new dashboard.** Old account references left from the Sprint 1 infra migration broke production images and took major unplanned effort to fix. That pain inspired the operational health dashboard - now being handed to Kay to productionize.
- **Google-registration bug** was a significant time sink (fix expected end of day) - a real driver of the carryover.
- **Seller module (from UAT)** is blocked on CEO input: broker-agreement update + white-glove service pricing. It keeps rolling over until that decision lands.

Velocity - Completed by Size

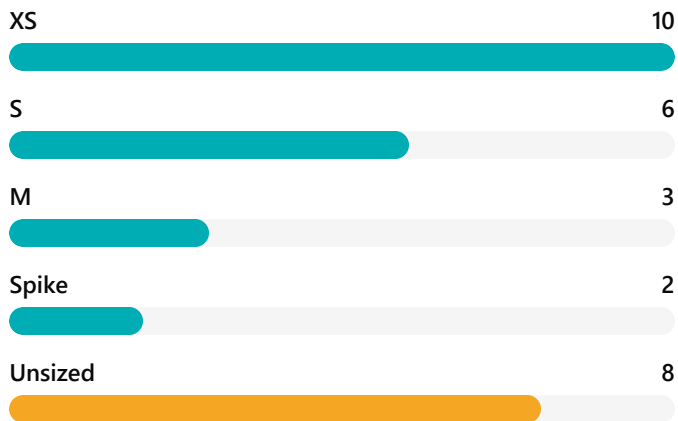

First sized baseline

The team delivered **21 sized items** (10 XS, 6 S, 3 M, 2 Spike) plus 8 unsized carryover. **No L or larger** was completed. This is the first throughput baseline; it sharpens each fully-sized sprint.

How We're Self-Correcting

From the retro

- To allocate dedicated time / open bugs for production
- sprints being only 1 week is tight especially in the summer time with holidays, move to 2 week sprint but still have weekly production releases as well as any hot fixes necessary

Actions next sprint

- Unblock the seller module (CEO: broker agreement + white-glove pricing)
- Protect tech-debt capacity (slipped 0/2 this sprint)
- Dedicated production-bug time

Sprint 3 Planning

TECHNICAL HARDENING SPRINT

Complete the Wompi switch, productionize the ops health dashboard, add GCP health, stand up code review + Jira/GitHub - plus ship "create a project from a visualization".

COMMITTED

40

11 carry · 12 new

READINESS

Ready

gate passed

SIZED

40/40


all sized

GOAL

Set

Wompi + technical

Committed Scope

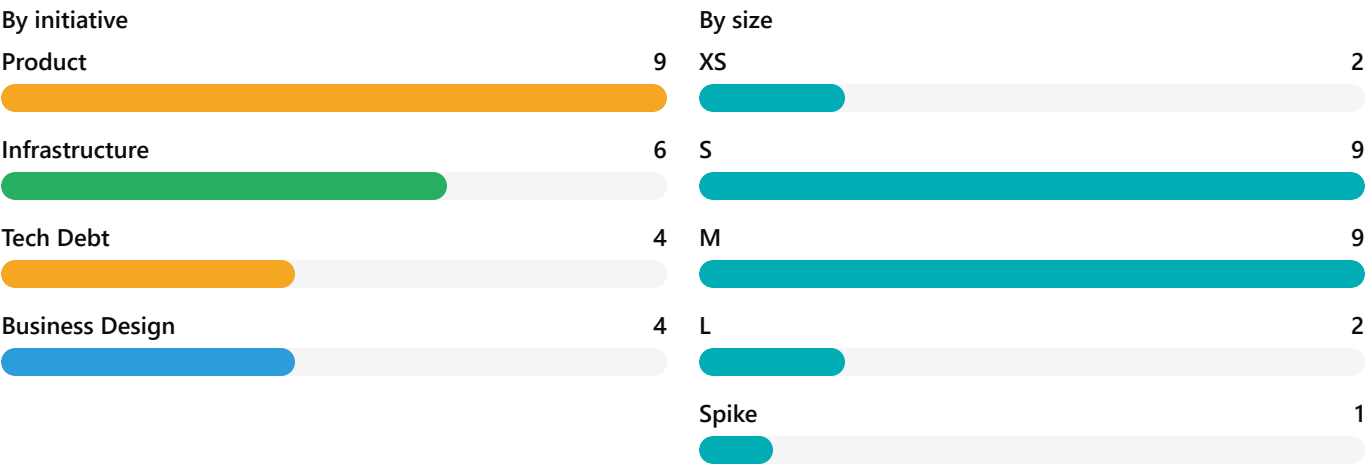

Capacity vs Last Sprint

Capacity watch. Sprint 3 commits 9 M and 2 L items; Sprint 2 delivered 3 M and 0 L. The committed mix is heavier than proven throughput - confirm capacity or trim the larger items before locking. Velocity baseline is one sprint old and partly unsized, so treat as directional.

SPRINT 3

What's in Scope

All 40 committed items. **CO** = carryover from Sprint 2.

Business Design (4)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-546	Story	L	In Prog	Charles	CO	Design for Supplier Catalogs
RAI-646	Story	M	To Do	David		Design Notification Emails
RAI-649	Story	M	To Do	Charles		Web Scraper to Hubspot Integration Setup
RAI-654	Story	L	To Do	Charles		Moodboard Design

Product (9)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-437	Story	S	QA	Charles	CO	Create Home Seller User Type
RAI-65	Story	M	QA	Kay	CO	Teams
RAI-608	Story	M	To Do	Kay	CO	Update Wompi Account to New ReformAI Bank Account
RAI-550	Bug	XS	To Do	Kay	CO	Service Providers: Update Subscription
RAI-650	Story	XS	To Do	Kay		Admin Dashboard Updates
RAI-652	Story	S	To Do	Kay		Bring back version of being able to scroll the platform without being...
RAI-653	Story	S	To Do	Charles		Test Team member functionality
RAI-622	Story	S	To Do	Kay	CO	Update Broker Agreement for White Glove Service in Legal Documents an...
RAI-656	Story	M	To Do	Kay		Review and Implement Creating a Project from Visualization

Tech Debt (4)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-582	Story	S	In Prog	Kay	CO	[LOGIC] Migrate hardcoded filter prices and ranges to database for mu...
RAI-560	Story	S	In Prog	Kay	CO	[Infra] Implement production error monitoring and alerting for Google...
RAI-587	Story	M	To Do	Kay		[TESTING] Implement automated test coverage for Wompi payment integra...
RAI-648	Story	M	To Do	Kay		Optimize and Implement Operations Health Dashboard

Infrastructure (6)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-630	Bug	S	In Prog	Kay	CO	Sign in with Google: If user hasn't registered before then need to ta...
RAI-651	Story	S	To Do	Kay		Optimize photos loading: Inspiration Hub and Renovation Game
RAI-467	Story	M	To Do	Kay		GCP: Install a function to determine cost per API call
RAI-579	Story	M	To Do	Kay	CO	[DATA] Establish automated database migration pipelines and rollback...
RAI-627	Story	Spike	To Do	Kay	CO	Implement Code Review in Github
RAI-644	Story	S	To Do	Kay		Implement Github/Jira Connection
