

SPRINT 3 · JUL 2026

Sprint 3 Review

Goal: technical hardening - Wompi switch, ops health + Google Cloud monitoring, code review, and create-a-project-from-a-visualization.

● SPRINT HEALTH: GREEN · GOAL MET**SPRINT GOAL****Met**

4 of 6 pillars done

COMPLETION**60%**

18 of 30 items

COMMITTED WORK**61%**

14 of 23 committed-at-start



CARRIED OVER**12**

Roll into Sprint 4

The Headline

The Wompi switch landed - 18 of 30 done (60%). Of the 23 items committed at sprint start, 14 shipped (61%); the team also absorbed 7 items added mid-sprint and finished 4 of them. The Sprint 2 external blocker is resolved, code review is stood up in GitHub, and the operational health dashboard is in production with Google Cloud monitoring added. Four of six goal pillars are complete; the other two are in progress, not missed.

Delivery at a Glance

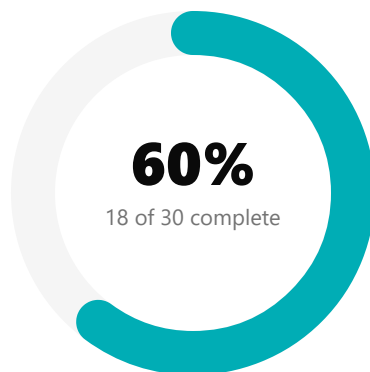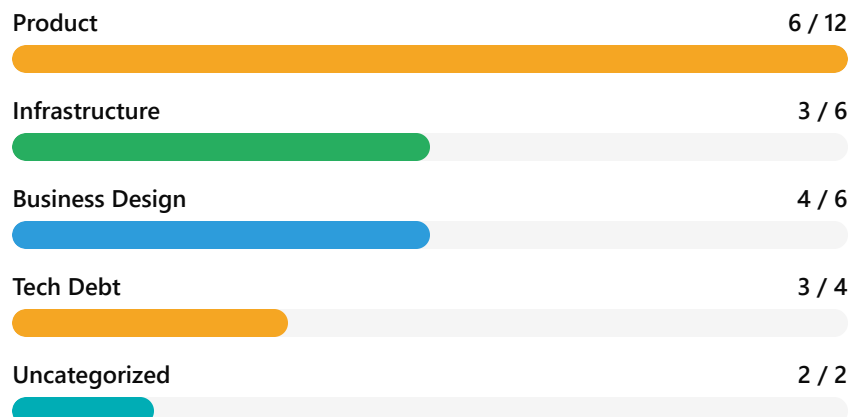**By initiative****By type:** Bugs 4 / 7 done · Stories 14 / 23 done.

What We Shipped & Why It Matters

WOMPI

Account switched to the ReformAI bank account

Goal

CODE REVIEW

Stood up in GitHub

Goal

OPS HEALTH

Operational health dashboard productionized

Goal

GCP MONITORING

Google Cloud health monitoring added

Goal

ASSET PIPELINE

Asset Discovery Pipeline shipped

Product

AIRBNB


Airbnb Investor Landing Page shipped

Product

The Story Behind the Numbers

- **Scope grew mid-sprint.** 7 items were added after the sprint started; the team completed 4. The 3 that carried over are all reactive homeowner-registration bugs - the reason a **Production Bugs bucket** now exists in Sprint 4.
- **Two UAT-era stories are still blocked on the CEO.** Create Home Seller User Type (RAI-437) and the White-Glove broker-agreement update (RAI-622) have carried since UAT, waiting on the broker-agreement decision and white-glove pricing. They will keep rolling over until that call is made.
- **Prod regressions from hotfixes.** Flagged in the retro; it motivates a per-build test suite and standard user-checks across all tabs and pages.
- **Supplier Catalog is hard to design** without enough client catalogs to generalize from. It carries into Sprint 4 and needs unblocking (sample catalogs, or a research spike) before more design effort.
- **Venezuela new-market design** pulled focus from sprint initiatives.

Velocity - Completed by Size

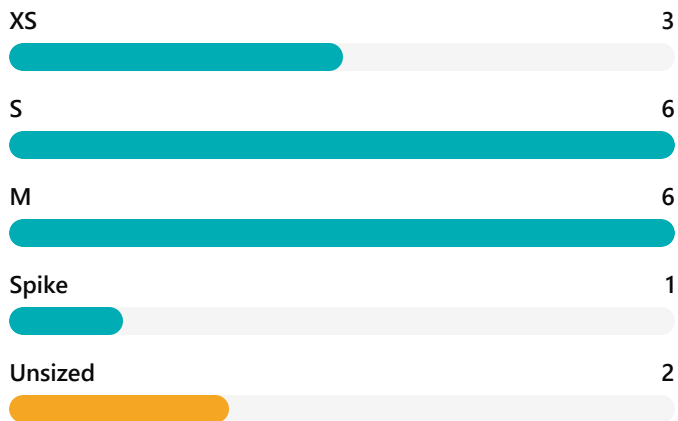

M throughput doubled

The team delivered **16 sized items** (3 XS, 6 S, 6 M, 1 Spike) plus 2 unsized. Mid-size (M) throughput **doubled versus Sprint 2** (3 → 6). **No L or larger** was completed - the second sprint running - which is the key input to Sprint 4 capacity.

How We're Self-Correcting

From the retro

- Need to have standard user checks for all tabs pages
- Test suite for each new build to complete

Actions next sprint

- Unblock Supplier Catalog before designing it (sample catalogs, or a spike)
- Stand up a per-build test suite to catch prod regressions
- Track ad-hoc bugs against the new Production Bugs bucket

Sprint 4 Planning

INFRASTRUCTURE + PARTNER UI + EMAIL

Compiled Infrastructure Report + GCP Visualization Insight + Partner Projects UI Overhaul + Productionize Email Notifications

COMMITTED

24

12 carry · 12 new

READINESS

Ready

gate passed

BUGS

Bucketed


unsized by design

GOAL

Set

infra + UI + email

Committed Scope

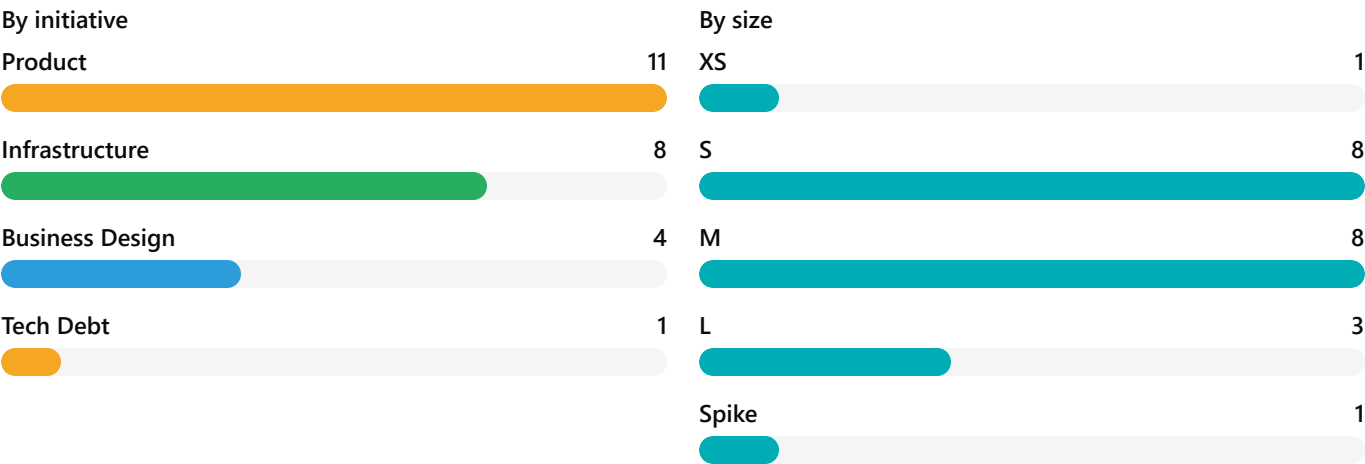

Capacity vs Last Sprint

Capacity watch. Sprint 4 commits 8 M and 3 L items; Sprint 3 delivered 6 M and 0 L (zero L). The committed mix is heavier than proven throughput - confirm capacity or trim/split the larger items before locking. The two carryover L's are Business Design (owner-acknowledged); RAI-546 (Supplier Catalog) is the one to watch, as the retro flagged it blocked.

SPRINT 4

What's in Scope

All 24 committed items. **CO** = carryover from Sprint 3.

Business Design (4)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-546	Story	L	In Prog	Charles	CO	Design for Supplier Catalogs
RAI-654	Story	L	To Do	Charles	CO	Moodboard Design
RAI-669	Story	M	To Do	David		Testing Notification Emails
RAI-675	Story	M	To Do	Charles		Design how Team Members login and Profile Pages

Product (11)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-437	Story	S	QA	Charles	CO	Create Home Seller User Type
RAI-656	Story	M	In Prog	Kay	CO	Review and Implement Creating a Project from Visualization
RAI-661	Bug	S	To Do	Kay	CO	Homeowner Registration Still has old Steps involved
RAI-666	Story	M	To Do	Kay		UI Changes for Partner Projects
RAI-668	Story	S	To Do	Kay		Inspiration Hub Updates
RAI-662	Bug	XS	To Do	Kay	CO	New Homeowner Registration is not showing up in New Users
RAI-664	Bug	S	To Do	Kay	CO	Admin Homeowner Account Updated to Premium
RAI-671	Story	S	To Do	Kay		Need to create a "Super Admin" and "Admin"
RAI-676	Story	S	To Do	Kay		Improvement on Photos Loading on Detail Page for Listings
RAI-622	Story	S	To Do	Kay	CO	Update Broker Agreement for White Glove Service in Legal Documents an...
RAI-678	Story	M	To Do	Kay		Production Bugs Sprint 4

Tech Debt (1)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-587	Story	M	To Do	Kay	CO	[TESTING] Implement automated test coverage for Wompi payment integra...

Infrastructure (8)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-467	Story	M	In Prog	Kay	CO	GCP: Install a function to determine cost per API call
RAI-677	Story	L	To Do	Kay		Create a report that compiles all infrastructure in one space so we c...
RAI-579	Story	M	To Do	Kay	CO	[DATA] Establish automated database migration pipelines and rollback...
RAI-644	Story	S	To Do	Kay	CO	Implement Github/Jira Connection
RAI-670	Story	Spike	To Do	Kay		Analyze what needs to be done to onboard a new market
RAI-674	Bug	-	To Do	Kay		Bug – Service Providers Cannot Load Available Projects (HTTP 500 Erro...
RAI-673	Bug	-	To Do	Kay		Regression – AI Image Generation Disabled in Partner Projects
RAI-672	Bug	-	To Do	Kay		Performance Issue – Property Images Load Slowly on Property Detail Pa...
