

SPRINT 2 · JUN 2026

Sprint 2 Review

Goal: switch Wompi billing to the ReformAI account and ship the 3 user dashboards.

● SPRINT HEALTH: GREEN · GOAL PARTIAL

SPRINT GOAL

Partial

Dashboards yes; Wompi pending

COMPLETION

72%

29 of 40 items

CARRIED OVER

11

Roll into Sprint 3

BEST YET


72%

Highest completion to date

The Headline

Strongest sprint to date - 29 of 40 done (72%). The 3 user dashboards shipped. The Wompi account switch is still pending on Wompi's side - an external dependency, not a team miss (the CEO met Wompi and the switch carries into Sprint 3). **Standout:** analytics was scoped only as a research task; the team found PostHog and fully implemented it in-sprint, ahead of plan.

Delivery at a Glance

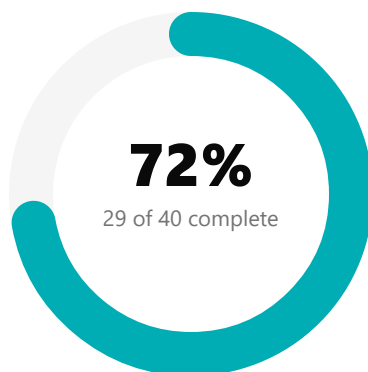

By initiative

Product 20 / 25

Infrastructure 5 / 8

Business Design 4 / 5

Tech Debt 0 / 2

By type: Bugs 13 / 15 done · Stories 15 / 24 done. Tech Debt slipped (0 of 2).

What We Shipped & Why It Matters

DASHBOARDS

3 user dashboards live

Goal

POSTHOG

Analytics found + shipped in-sprint

Ahead of plan

OPS HEALTH

New operational health dashboard

Infrastructure

EMAIL

Notification templates for every user type

Visuals this sprint

ADMIN LOGS

User activity logs in the admin module

Product

PLATFORM


Landing pages live + email notifications

Product

The Story Behind the Numbers

- **Cloudflare fallout -> a new dashboard.** Old account references left from the Sprint 1 infra migration broke production images and took major unplanned effort to fix. That pain inspired the operational health dashboard - now being handed to Kay to productionize.
- **Google-registration bug** was a significant time sink (fix expected end of day) - a real driver of the carryover.
- **Seller module (from UAT)** is blocked on CEO input: broker-agreement update + white-glove service pricing. It keeps rolling over until that decision lands.

Velocity - Completed by Size

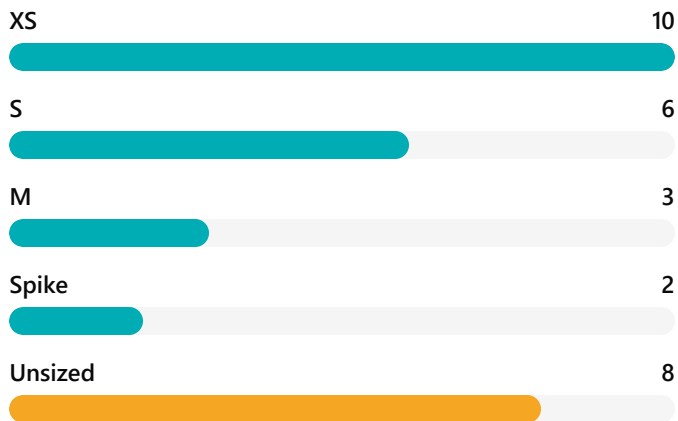

First sized baseline

The team delivered **21 sized items** (10 XS, 6 S, 3 M, 2 Spike) plus 8 unsized carryover. **No L or larger** was completed. This is the first throughput baseline; it sharpens each fully-sized sprint.

How We're Self-Correcting

From the retro

- To allocate dedicated time / open bugs for production
- sprints being only 1 week is tight especially in the summer time with holidays, move to 2 week sprint but still have weekly production releases as well as any hot fixes necessary

Actions next sprint

- Unblock the seller module (CEO: broker agreement + white-glove pricing)
- Protect tech-debt capacity (slipped 0/2 this sprint)
- Dedicated production-bug time

Sprint 3 Planning

TECHNICAL HARDENING SPRINT

Complete the Wompi switch, productionize the ops health dashboard, add GCP health, stand up code review + Jira/GitHub - plus ship "create a project from a visualization".

COMMITTED

23

11 carry · 12 new

READINESS

Ready

gate passed

SIZED

23/23


all sized

GOAL

Set

Wompi + technical

Committed Scope

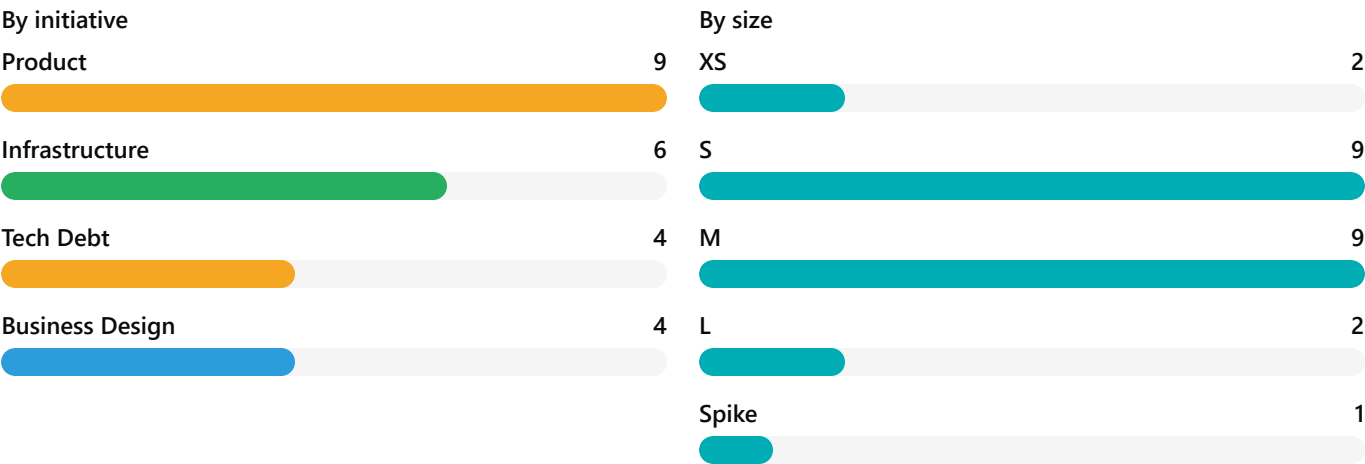

Capacity vs Last Sprint

Capacity watch.

Sprint 3 commits 9 M and 2 L items; Sprint 2 delivered 3 M and 0 L. The committed mix is heavier than proven throughput - confirm capacity or trim the larger items before locking. Velocity baseline is one sprint old and partly unsized, so treat as directional.

SPRINT 3

What's in Scope

All 23 committed items. **CO** = carryover from Sprint 2.

Business Design (4)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-546	Story	L	In Prog	Charles	CO	Design for Supplier Catalogs
RAI-646	Story	M	To Do	David		Design Notification Emails
RAI-649	Story	M	To Do	Charles		Web Scraper to Hubspot Integration Setup
RAI-654	Story	L	To Do	Charles		Moodboard Design

Product (9)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-437	Story	S	QA	Charles	CO	Create Home Seller User Type
RAI-65	Story	M	QA	Kay	CO	Teams
RAI-608	Story	M	To Do	Kay	CO	Update Wompi Account to New ReformAI Bank Account
RAI-550	Bug	XS	To Do	Kay	CO	Service Providers: Update Subscription
RAI-650	Story	XS	To Do	Kay		Admin Dashboard Updates
RAI-652	Story	S	To Do	Kay		Bring back version of being able to scroll the platform without being registered
RAI-653	Story	S	To Do	Charles		Test Team member functionality
RAI-622	Story	S	To Do	Kay	CO	Update Broker Agreement for White Glove Service in Legal Documents and During Registration
RAI-656	Story	M	To Do	Kay		Review and Implement Creating a Project from Visualization

Tech Debt (4)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-582	Story	S	In Prog	Kay	CO	[LOGIC] Migrate hardcoded filter prices and ranges to database for multi-currency/country support
RAI-560	Story	S	In Prog	Kay	CO	[Infra] Implement production error monitoring and alerting for Google Cloud Run
RAI-587	Story	M	To Do	Kay		[TESTING] Implement automated test coverage for Wompi payment integration
RAI-648	Story	M	To Do	Kay		Optimize and Implement Operations Health Dashboard

Infrastructure (6)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-630	Bug	S	In Prog	Kay	CO	Sign in with Google: If user hasn't registered before then need to take them to register page
RAI-651	Story	S	To Do	Kay		Optimize photos loading: Inspiration Hub and Renovation Game
RAI-467	Story	M	To Do	Kay		GCP: Install a function to determine cost per API call
RAI-579	Story	M	To Do	Kay	CO	[DATA] Establish automated database migration pipelines and rollback strategies
RAI-627	Story	Spike	To Do	Kay	CO	Implement Code Review in Github
RAI-644	Story	S	To Do	Kay		Implement Github/Jira Connection
