

SPRINT 2 · JUN 2026

Sprint 2 Review

Goal: switch Wompi billing to the ReformAI account and ship the 3 user dashboards.

● SPRINT HEALTH: GREEN · GOAL PARTIAL

SPRINT GOAL

Partial

Dashboards yes; Wompi pending

COMPLETION

72%

29 of 40 items

CARRIED OVER

11

Roll into Sprint 3

BEST YET


72%

Highest completion to date

The Headline


Strongest sprint to date - 29 of 40 done (72%). The 3 user dashboards shipped. The Wompi account switch is still pending on Wompi's side - an external dependency, not a team miss (the CEO met Wompi and the switch carries into Sprint 3). **Standout:** analytics was scoped only as a research task; the team found PostHog and fully implemented it in-sprint, ahead of plan.

Delivery at a Glance

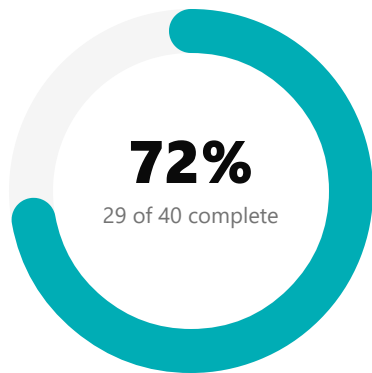

Reform-A.i · Sprint 2 Review

By initiative

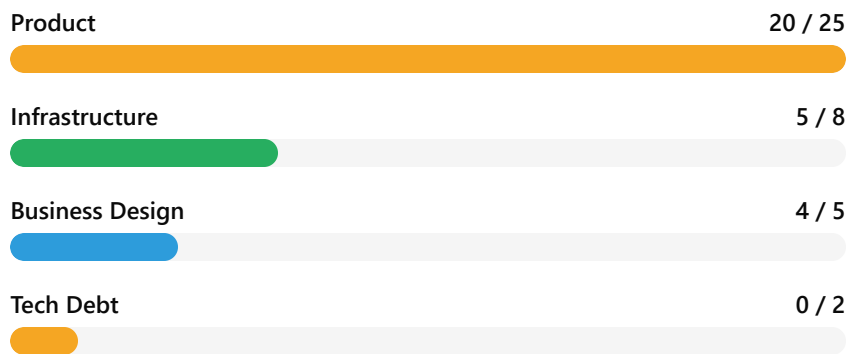

By type: Bugs 13 / 15 done · Stories 15 / 24 done. Tech Debt slipped (0 of 2).
Confidential

| What We Shipped & Why It Matters

DASHBOARDS

3 user dashboards live

Goal

POSTHOG

Analytics found + shipped in-sprint

Ahead of plan

OPS HEALTH

New operational health dashboard

Infrastructure

PLATFORM


Email notifications + landing pages live

Product

| The Story Behind the Numbers

- **Cloudflare fallout -> a new dashboard.** Old account references left from the Sprint 1 infra migration broke production images and took major unplanned effort to fix. That pain inspired the operational health dashboard - now being handed to Kay to productionize.
- **Google-registration bug** was a significant time sink (fix expected end of day) - a real driver of the carryover.
- **Seller module (from UAT)** is blocked on CEO input: broker-agreement update + white-glove service pricing. It keeps rolling over until that decision lands.

| Velocity - Completed by Size

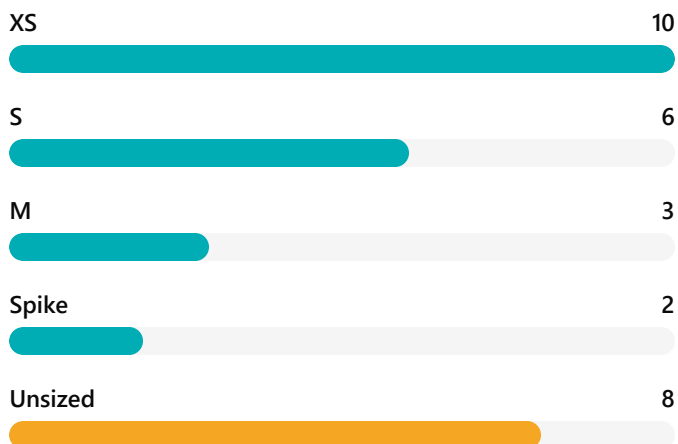

First sized baseline

The team delivered **21 sized items** (10 XS, 6 S, 3 M, 2 Spike) plus 8 unsized carryover. **No L or larger** was completed. This is the first throughput baseline; it sharpens each fully-sized sprint.

| How We're Self-Correcting

From the retro

- To allocate dedicated time / open bugs for production

Actions next sprint

- Unblock the seller module (CEO: broker agreement + white-glove pricing)
- Protect tech-debt capacity (slipped 0/2 this sprint)

- sprints being only 1 week is tight especially in the summer time with holidays, move to 2 week sprint but still have weekly production releases as well as any hot fixes necessary

- Dedicated production-bug time

Sprint 3 Planning

TECHNICAL HARDENING SPRINT

Complete the Wompi switch, productionize the ops health dashboard, add GCP health, stand up code review + Jira/GitHub - plus ship "create a project from a visualization".

COMMITTED

23

11 carry · 12 new

READINESS

Ready

gate passed

SIZED

23/23


all sized

GOAL

Set

Wompi + technical

Committed Scope

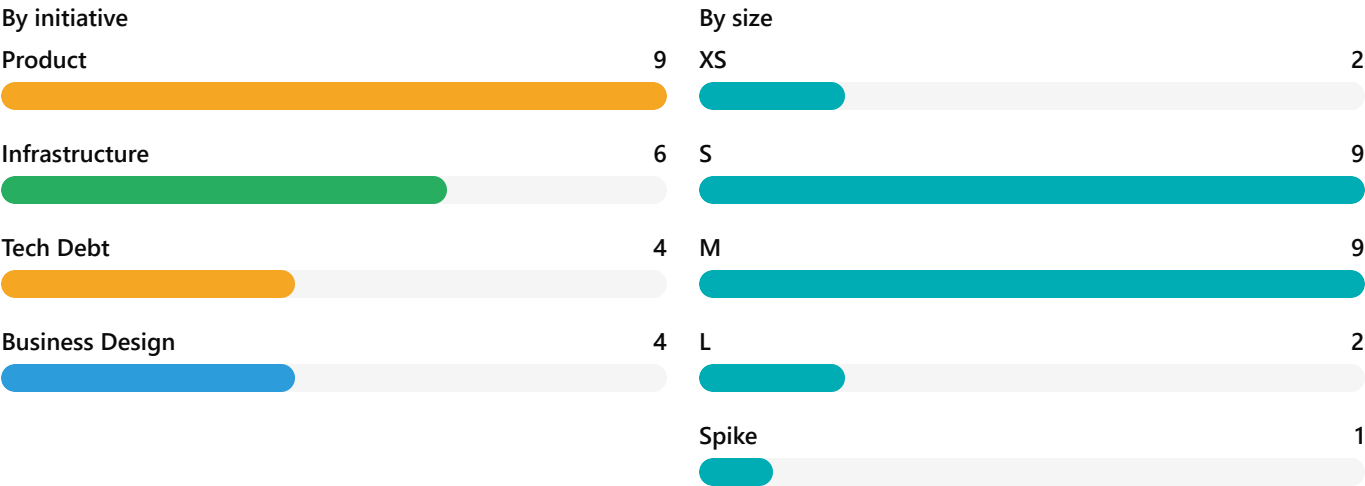

Capacity vs Last Sprint

Capacity watch. Sprint 3 commits 9 M and 2 L items; Sprint 2 delivered 3 M and 0 L. The committed mix is heavier than proven throughput - confirm capacity or trim the larger items before locking. Velocity baseline is one sprint old and partly unsized, so treat as directional.

SPRINT 3

What's in Scope

All 23 committed items. **CO** = carryover from Sprint 2.

Business Design (4)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-546	Story	L	In Prog	Charles	CO	Design for Supplier Catalogs
RAI-646	Story	M	To Do	David		Design Notification Emails
RAI-649	Story	M	To Do	Charles		Web Scraper to Hubspot Integration Setup
RAI-654	Story	L	To Do	Charles		Moodboard Design

Product (9)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-437	Story	S	QA	Charles	CO	Create Home Seller User Type
RAI-65	Story	M	QA	Kay	CO	Teams
RAI-608	Story	M	To Do	Kay	CO	Update Wompi Account to New ReformAI Bank Account
RAI-550	Bug	XS	To Do	Kay	CO	Service Providers: Update Subscription
RAI-650	Story	XS	To Do	Kay		Admin Dashboard Updates
RAI-652	Story	S	To Do	Kay		Bring back version of being able to scroll the platform without being registered
RAI-653	Story	S	To Do	Charles		Test Team member functionality
RAI-622	Story	S	To Do	Kay	CO	Update Broker Agreement for White Glove Service in Legal Documents and During Registration
RAI-656	Story	M	To Do	Kay		Review and Implement Creating a Project from Visualization

Tech Debt (4)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-582	Story	S	In Prog	Kay	CO	[LOGIC] Migrate hardcoded filter prices and ranges to database for multi-currency/country support
RAI-560	Story	S	In Prog	Kay	CO	[Infra] Implement production error monitoring and alerting for Google Cloud Run
RAI-587	Story	M	To Do	Kay		[TESTING] Implement automated test coverage for Wompi payment integration
RAI-648	Story	M	To Do	Kay		Optimize and Implement Operations Health Dashboard

Infrastructure (6)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-630	Bug	S	In Prog	Kay	CO	Sign in with Google: If user hasn't registered before then need to take them to register page
RAI-651	Story	S	To Do	Kay		Optimize photos loading: Inspiration Hub and Renovation Game
RAI-467	Story	M	To Do	Kay		GCP: Install a function to determine cost per API call
RAI-579	Story	M	To Do	Kay	CO	[DATA] Establish automated database migration pipelines and rollback strategies
RAI-627	Story	Spike	To Do	Kay	CO	Implement Code Review in Github
RAI-644	Story	S	To Do	Kay		Implement Github/Jira Connection
