

SPRINT 3 · JUL 2026

Revisión Sprint 3

Objetivo: fortalecimiento técnico - cambio de Wompi, salud operativa + monitoreo de Google Cloud, revisión de código, y crear-un-proyecto-desde-una-visualización.


● ESTADO DEL SPRINT: VERDE · OBJETIVO MAYORMENTE CUMPLIDO



Lo Más Importante

El cambio de Wompi se completó - 18 de 30 hechos (60%). De los 23 ítems comprometidos al inicio del sprint, 14 se entregaron (61%); el equipo además absorbió 7 ítems añadidos a mitad del sprint y terminó 4. El bloqueador externo del Sprint 2 está resuelto, la revisión de código está montada en GitHub, y el tablero de salud operativa está en producción con monitoreo de Google Cloud. Cuatro de seis pilares del objetivo están completos; los otros dos están en progreso, no fallidos.

Entrega de un Vistazo

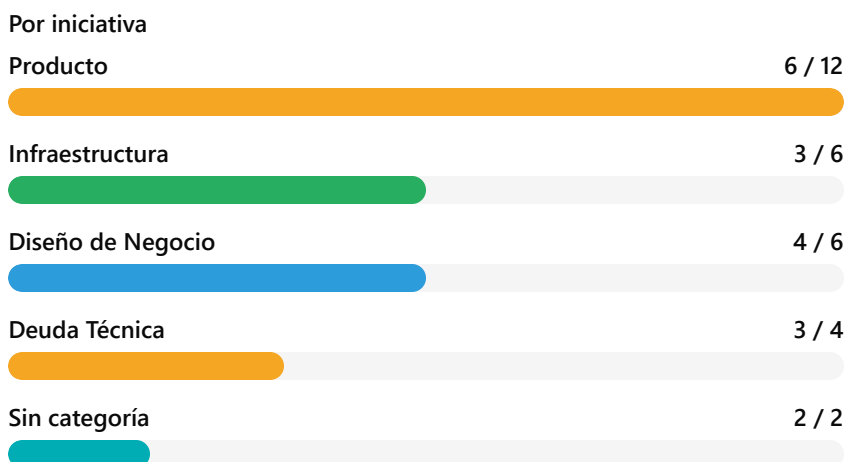

Por tipo: Bugs 4 / 7 hechos · Historias 14 / 23 hechas.

Lo Que Entregamos y Por Qué Importa

WOMPI

Cuenta cambiada a la cuenta bancaria de ReformAI

Objetivo

REVISIÓN DE CÓDIGO

Montada en GitHub

Objetivo

SALUD OPS

Tablero de salud operativa en producción

Objetivo

MONITOREO GCP

Monitoreo de salud de Google Cloud añadido

Objetivo

PIPELINE DE ACTIVOS

Asset Discovery Pipeline entregado

Producto

AIRBNB


Landing Page de Inversor Airbnb entregada

Producto

La Historia Detrás de los Números

- **El alcance creció a mitad del sprint.** Se añadieron 7 ítems después de iniciar el sprint; el equipo completó 4. Los 3 que se trasladaron son bugs reactivos de registro de propietarios - la razón por la que ahora existe un **bucket de Bugs de Producción** en el Sprint 4.
- **La creación de proyecto desde una visualización pasa al Sprint 4 como objetivo principal.** Entregada parcialmente en el Sprint 3 y ahora en el ambiente de QA; llevarla a producción es la primera prioridad del Sprint 4.
- **Dos historias de la época de UAT siguen bloqueadas por el CEO.** Crear Tipo de Usuario Vendedor (RAI-437) y la actualización del acuerdo de corretaje White-Glove (RAI-622) se han trasladado desde UAT, esperando la decisión del acuerdo de corretaje y los precios White-Glove. Recomendación: si el acuerdo de corretaje y los precios no se definen, retirar la funcionalidad del Módulo de Vendedor (RAI-437) de la aplicación hasta que se definan, en vez de exponer funcionalidad de vendedor sin los términos legales y de precios establecidos.
- **Regresiones en producción por hotfixes.** Señalado en la retro; motiva una suite de pruebas por cada build y verificaciones de usuario estándar en todas las pestañas y páginas.
- **El Catálogo de Proveedores pasó a un spike de investigación.** La retro señaló que es difícil de diseñar sin suficientes catálogos de clientes para generalizar; para el Sprint 4 pasa de historia grande a spike - reduciendo el riesgo mientras reunimos catálogos de muestra para diseñar.
- **El diseño del nuevo mercado de Venezuela** desvió el foco de las iniciativas del sprint.

Velocidad - Completado por Tamaño

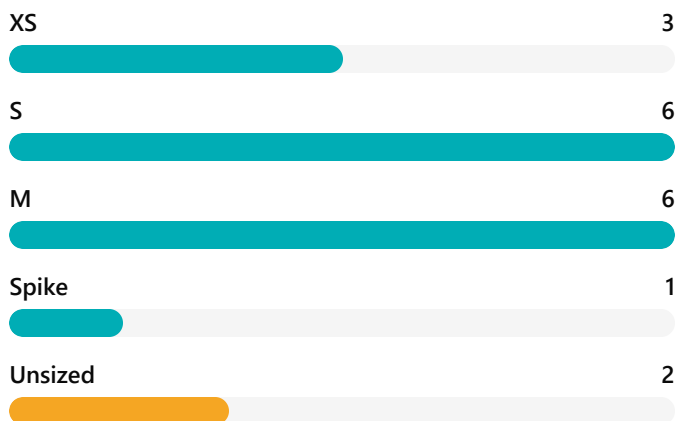

El rendimiento de M se duplicó

El equipo entregó **16 ítems con tamaño** (3 XS, 6 S, 6 M, 1 Spike) más 2 sin tamaño. El rendimiento de tamaño medio (M) **se duplicó versus el Sprint 2** (3 → 6). **No se completó ningún L o mayor** - el segundo sprint consecutivo - lo cual es el insumo clave para la capacidad del Sprint 4.

Cómo Nos Auto-Corregimos

De la retro

- Need to have standard user checks for all tabs pages
- Test suite for each new build to complete

Acciones próximo sprint

- El Catálogo de Proveedores pasó a un spike de investigación; reunir catálogos de clientes de muestra para diseñar
- Montar una suite de pruebas por cada build para detectar regresiones en producción
- Rastrear bugs ad-hoc contra el nuevo bucket de Bugs de Producción

Planeación Sprint 4

PROYECTO-DESDE-VISUALIZACIÓN + INFRA + UI DE SOCIOS + CORREO

Creación de Proyecto desde Visualización en Producción + Reporte de Infraestructura Compilado + Análisis de Visualización GCP + Renovación de UI de Proyectos de Socios + Productivizar Notificaciones por Correo

COMPROMETIDO

24

12 traslado · 12 nuevos

PREPARACIÓN

Listo

filtro aprobado

BUGS

En bucket


sin tamaño por diseño

OBJETIVO

Definido

liderado por traslados

Alcance Comprometido

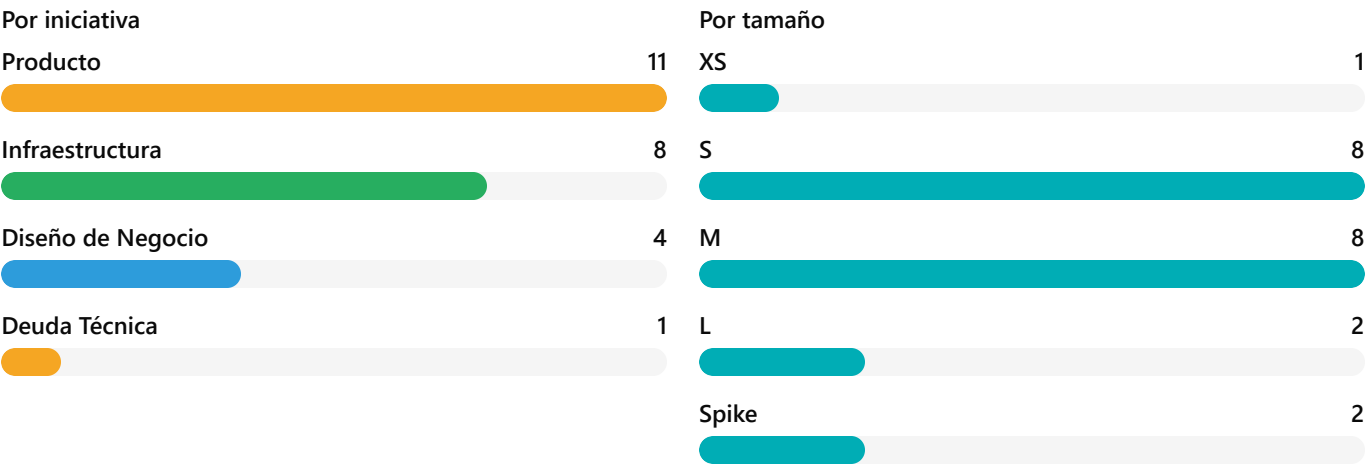

Capacidad vs Sprint Anterior

Alerta de capacidad. El Sprint 4 compromete 8 M y 2 L; el Sprint 3 entregó 6 M y 0 L (cero L). La carga de tamaño alto bajó este ciclo: el Catálogo de Proveedores (RAI-546) pasó de historia grande a spike de investigación, reduciendo el conteo de L a 2. Los L restantes son el reporte de infraestructura (RAI-677, un ancla del objetivo) y el Diseño de Moodboard (RAI-654). Aún confirme la capacidad de M - 8 M está por encima de los 6 entregados el sprint pasado.

SPRINT 4

Qué Está en el Alcance

Los 24 ítems comprometidos. co = trasladado del Sprint 3.

Diseño de Negocio (4)

CLAVE	TIPO	TAMAÑO	ESTADO	RESPONSABLE	RESUMEN
RAI-546	Story	Spike	En Curso	Charles	co Design for Supplier Catalogs
RAI-654	Story	L	Por Hacer	Charles	co Moodboard Design
RAI-669	Story	M	Por Hacer	David	Testing Notification Emails
RAI-675	Story	M	Por Hacer	Charles	Design how Team Members login and Profile Pages

Producto (11)

CLAVE	TIPO	TAMAÑO	ESTADO	RESPONSABLE	RESUMEN
RAI-437	Story	S	QA	Charles	co Create Home Seller User Type
RAI-656	Story	M	En Curso	Kay	co Review and Implement Creating a Project from Visualization
RAI-661	Bug	S	Por Hacer	Kay	co Homeowner Registration Still has old Steps involved
RAI-666	Story	M	Por Hacer	Kay	UI Changes for Partner Projects
RAI-668	Story	S	Por Hacer	Kay	Inspiration Hub Updates
RAI-662	Bug	XS	Por Hacer	Kay	co New Homeowner Registration is not showing up in New Users
RAI-664	Bug	S	Por Hacer	Kay	co Admin Homeowner Account Updated to Premium
RAI-671	Story	S	Por Hacer	Kay	Need to create a "Super Admin" and "Admin"
RAI-676	Story	S	Por Hacer	Kay	Improvement on Photos Loading on Detail Page for Listings
RAI-622	Story	S	Por Hacer	Kay	co Update Broker Agreement for White Glove Service in Legal Documents an...
RAI-678	Story	M	Por Hacer	Kay	Production Bugs Sprint 4

Deuda Técnica (1)

CLAVE	TIPO	TAMAÑO	ESTADO	RESPONSABLE	RESUMEN
RAI-587	Story	M	Por Hacer	Kay	co [TESTING] Implement automated test coverage for Wompi payment integra...

Infraestructura (8)

CLAVE	TIPO	TAMAÑO	ESTADO	RESPONSABLE	RESUMEN
RAI-467	Story	M	En Curso	Kay	co GCP: Install a function to determine cost per API call
RAI-677	Story	L	Por Hacer	Kay	Create a report that compiles all infrastructure in one space so we c...
RAI-579	Story	M	Por Hacer	Kay	co [DATA] Establish automated database migration pipelines and rollback...
RAI-644	Story	S	Por Hacer	Kay	co Implement Github/Jira Connection
RAI-670	Story	Spike	Por Hacer	Kay	Analyze what needs to be done to onboard a new market
RAI-674	Bug	-	Por Hacer	Kay	Bug – Service Providers Cannot Load Available Projects (HTTP 500 Erro...
RAI-673	Bug	-	Por Hacer	Kay	Regression – AI Image Generation Disabled in Partner Projects
RAI-672	Bug	-	Por Hacer	Kay	Performance Issue – Property Images Load Slowly on Property Detail Pa...

SPRINT 3 · JUL 2026

Sprint 3 Review

Goal: technical hardening - Wompi switch, ops health + Google Cloud monitoring, code review, and create-a-project-from-a-visualization.

● SPRINT HEALTH: GREEN · GOAL SUBSTANTIALY MET

SPRINT GOAL

4 / 6

pillars complete

COMPLETION

60%

18 of 30 items

COMMITTED WORK

61%

14 of 23 committed-at-start

CARRIED OVER


12

Roll into Sprint 4


The Headline

The Wompi switch landed - 18 of 30 done (60%). Of the 23 items committed at sprint start, 14 shipped (61%); the team also absorbed 7 items added mid-sprint and finished 4 of them. The Sprint 2 external blocker is resolved, code review is stood up in GitHub, and the operational health dashboard is in production with Google Cloud monitoring added. Four of six goal pillars are complete; the other two are in progress, not missed.

Delivery at a Glance

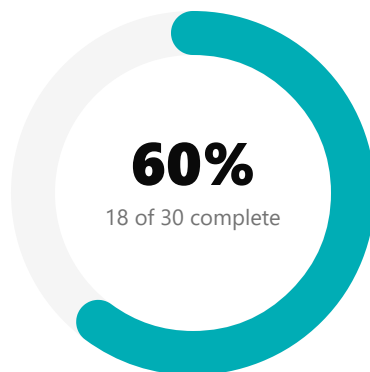

By initiative

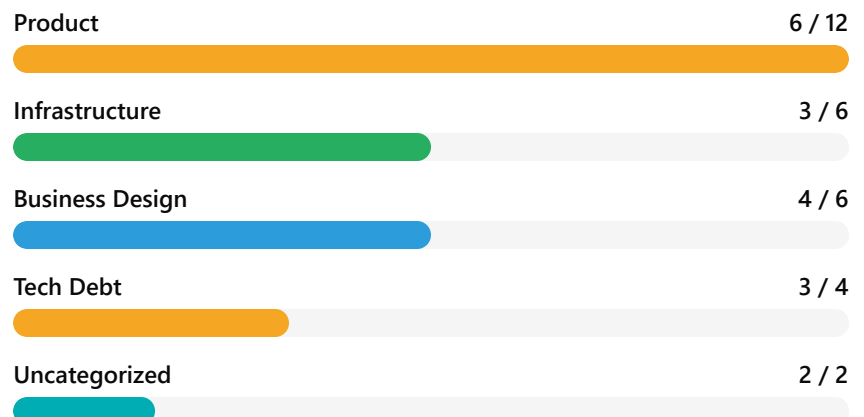

By type: Bugs 4 / 7 done · Stories 14 / 23 done.

What We Shipped & Why It Matters

WOMPI

Account switched to the ReformAI bank account

Goal

CODE REVIEW

Stood up in GitHub

Goal

OPS HEALTH

Operational health dashboard productionized

Goal

GCP MONITORING

Google Cloud health monitoring added

Goal

ASSET PIPELINE

Asset Discovery Pipeline shipped

Product

AIRBNB


Airbnb Investor Landing Page shipped

Product

The Story Behind the Numbers

- **Scope grew mid-sprint.** 7 items were added after the sprint started; the team completed 4. The 3 that carried over are all reactive homeowner-registration bugs - the reason a **Production Bugs bucket** now exists in Sprint 4.
- **Project creation from a visualization carries into Sprint 4 as the top goal.** Partially delivered in Sprint 3 and now in the QA environment; taking it to production is Sprint 4's first priority.
- **Two UAT-era stories are still blocked on the CEO.** Create Home Seller User Type (RAI-437) and the White-Glove broker-agreement update (RAI-622) have carried since UAT, waiting on the broker-agreement decision and white-glove pricing. Recommendation: if the broker agreement and pricing are not settled, pull the Seller Module feature (RAI-437) from the application until they are, rather than exposing seller functionality without the legal and pricing terms in place.
- **Prod regressions from hotfixes.** Flagged in the retro; it motivates a per-build test suite and standard user-checks across all tabs and pages.
- **Supplier Catalog moved to a research spike.** The retro flagged it hard to design without enough client catalogs to generalize from; for Sprint 4 it converts from a large story to a spike - de-risking the effort while we gather sample catalogs to design against.
- **Venezuela new-market design** pulled focus from sprint initiatives.

Velocity - Completed by Size

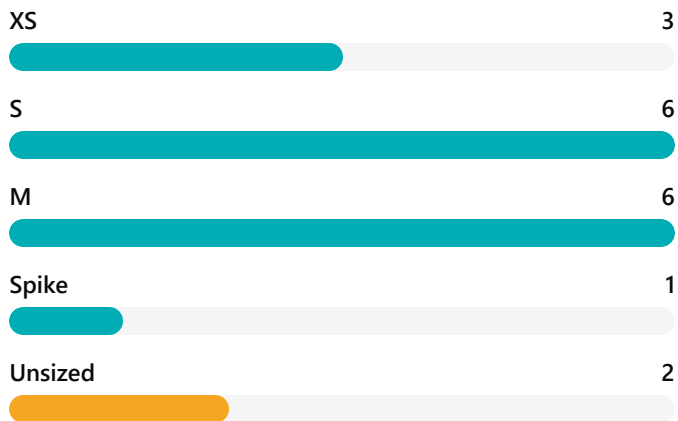

M throughput doubled

The team delivered **16 sized items** (3 XS, 6 S, 6 M, 1 Spike) plus 2 unsized. Mid-size (M) throughput **doubled versus Sprint 2** (3 → 6). **No L or larger** was completed - the second sprint running - which is the key input to Sprint 4 capacity.

How We're Self-Correcting

From the retro

- Need to have standard user checks for all tabs pages
- Test suite for each new build to complete

Actions next sprint

- Supplier Catalog moved to a research spike; gather sample client catalogs to design against
- Stand up a per-build test suite to catch prod regressions
- Track ad-hoc bugs against the new Production Bugs bucket

Sprint 4 Planning

PROJECT-FROM-VISUALIZATION + INFRA + PARTNER UI + EMAIL

Project Creation from Visualization in Production + Compiled Infrastructure Report + GCP Visualization Insight + Partner Projects UI Overhaul + Productionize Email Notifications

COMMITTED

24

12 carry · 12 new

READINESS

Ready

gate passed

BUGS

Bucketed


unsized by design

GOAL

Set

carryover-led

Committed Scope

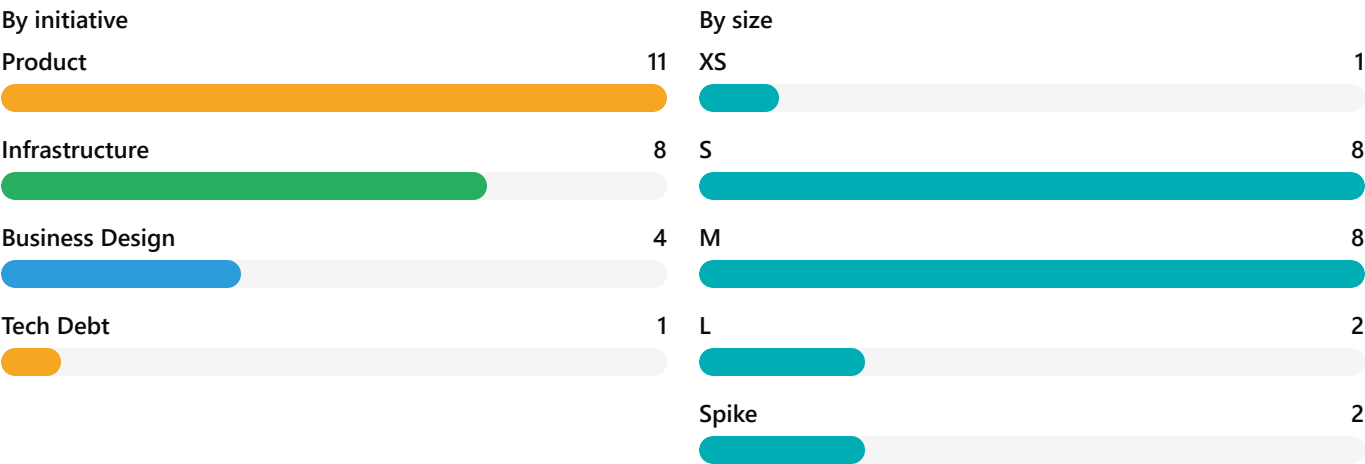

Capacity vs Last Sprint

Capacity watch. Sprint 4 commits 8 M and 2 L items; Sprint 3 delivered 6 M and 0 L (zero L). Top-end load eased this cycle: Supplier Catalog (RAI-546) was converted from a large story to a research spike, dropping the L count to 2. The remaining L's are the infrastructure report (RAI-677, a goal anchor) and Moodboard Design (RAI-654). Still confirm M capacity - 8 M sits above the 6 delivered last sprint.

SPRINT 4

What's in Scope

All 24 committed items. **CO** = carryover from Sprint 3.

Business Design (4)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-546	Story	Spike	In Prog	Charles	CO	Design for Supplier Catalogs
RAI-654	Story	L	To Do	Charles	CO	Moodboard Design
RAI-669	Story	M	To Do	David		Testing Notification Emails
RAI-675	Story	M	To Do	Charles		Design how Team Members login and Profile Pages

Product (11)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-437	Story	S	QA	Charles	CO	Create Home Seller User Type
RAI-656	Story	M	In Prog	Kay	CO	Review and Implement Creating a Project from Visualization
RAI-661	Bug	S	To Do	Kay	CO	Homeowner Registration Still has old Steps involved
RAI-666	Story	M	To Do	Kay		UI Changes for Partner Projects
RAI-668	Story	S	To Do	Kay		Inspiration Hub Updates
RAI-662	Bug	XS	To Do	Kay	CO	New Homeowner Registration is not showing up in New Users
RAI-664	Bug	S	To Do	Kay	CO	Admin Homeowner Account Updated to Premium
RAI-671	Story	S	To Do	Kay		Need to create a "Super Admin" and "Admin"
RAI-676	Story	S	To Do	Kay		Improvement on Photos Loading on Detail Page for Listings
RAI-622	Story	S	To Do	Kay	CO	Update Broker Agreement for White Glove Service in Legal Documents an...
RAI-678	Story	M	To Do	Kay		Production Bugs Sprint 4

Tech Debt (1)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-587	Story	M	To Do	Kay	CO	[TESTING] Implement automated test coverage for Wompi payment integra...

Infrastructure (8)

KEY	TYPE	SIZE	STATUS	OWNER		SUMMARY
RAI-467	Story	M	In Prog	Kay	CO	GCP: Install a function to determine cost per API call
RAI-677	Story	L	To Do	Kay		Create a report that compiles all infrastructure in one space so we c...
RAI-579	Story	M	To Do	Kay	CO	[DATA] Establish automated database migration pipelines and rollback...
RAI-644	Story	S	To Do	Kay	CO	Implement Github/Jira Connection
RAI-670	Story	Spike	To Do	Kay		Analyze what needs to be done to onboard a new market
RAI-674	Bug	-	To Do	Kay		Bug – Service Providers Cannot Load Available Projects (HTTP 500 Erro...
RAI-673	Bug	-	To Do	Kay		Regression – AI Image Generation Disabled in Partner Projects
RAI-672	Bug	-	To Do	Kay		Performance Issue – Property Images Load Slowly on Property Detail Pa...
