

SPRINT 1 · JUN 1 – JUN 5, 2026

Sprint 1 Review

Goal: transition infrastructure ownership from the offshore team to Reform-A.i.

● SPRINT HEALTH: GREEN · GOAL ACHIEVED

SPRINT GOAL

Achieved

Infra transition landed

COMPLETION

45%

13 of 29 work items

CARRIED OVER

16

Deprioritized by design

OPEN BLOCKERS


0

All clear

The Headline

We set out to move our infrastructure in-house, and we did it. The core transition off the offshore (Asymmetri) team to Reform-A.i landed (RAI-552), backed by Google Cloud Secret Manager (RAI-559) and per-push code versioning (RAI-624). That foundational work ran heavier than estimated, so we made a deliberate call: protect the goal and consciously push lower-priority stories to Sprint 2. The result is a lower raw completion number that represents a *won* sprint, not a missed one.

Delivery at a Glance

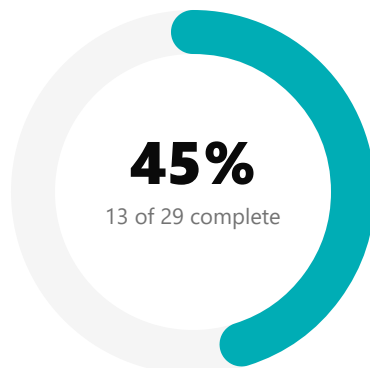


Infrastructure — the goal 2 / 2



Tech Debt 2 / 3



Product (Stories + Bugs) 9 / 24



By work type: Bugs 8 / 16 done · Stories 5 / 13 done. Bugs led delivery while the team focused capacity on the infrastructure stories.

What We Shipped

RAI-552

Infrastructure moved to Reform-A.i

Infrastructure · Goal

RAI-559

GCP Secret Manager + centralized env vars

Tech Debt

RAI-624

Per-push code-set version control

Infrastructure

RAI-594

DB-backed legal documents with Admin UI

Tech Debt

Plus production fixes: Partner Projects errors, Spanish localization, contract creation, and the seller/supplier user-type bug — 13 items completed in total.

How We're Self-Correcting

Retro action items

Document Slack/Jira ticket-submission process



Research automated testing (Cypress)



Research user-tracking tooling



GitHub/Jira integration



Implement code review in GitHub



Process improvements next sprint

- Adopt t-shirt sizing on every item for real capacity planning
- Budget goal-work capacity first, then add stories
- Add release rollback capability (already queued in Sprint 2)
- Surface and clear blockers mid-sprint, not at close
- Record the sprint goal in Jira for automatic health

Risk Watch

No open blockers. Every Sprint 1 item is either shipped or actively in flight heading into Sprint 2 — a clean handoff.

Sprint 2 Planning

JUN 9 – JUN 15, 2026

Goal: Wompi Account Update & Dashboard Views

COMMITTED

31

20 stories / 11 bugs

SIZED

28 / 31

3 unsized are Done

CARRYOVER

19


only 9 net-new

READINESS

Ready

gate passed

Committed Scope

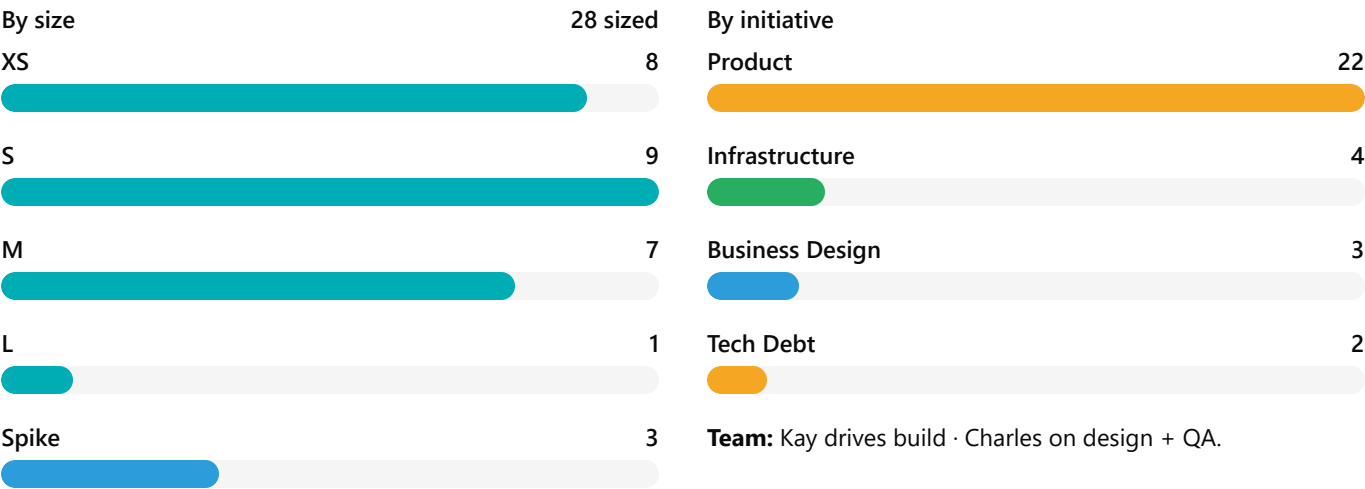

Readiness & Watch

Plan-ready

- All 31 items linked to an epic
- All active items t-shirt sized
- All active items have an owner

Planning watch

19 of 31 items are carryover from Sprint 1 — only 9 are net-new. Sprint 2 is largely about finishing the work that was deliberately deprioritized to land Sprint 1's goal. Watch for piling new scope on top of a 19-item backlog.
